

The Gallery pages below scroll backward in time.



To see a video of the construction site, return to Building Project home page and click on photo with this symbol in the middle

August 24-27, 2020

Going on this week: Continuing work on cement-block foundation walls

Remember the half-finished wall from last week? Here it is now!

Here it is from the opposite side!

Here it is from the far west end!








To see a video of the construction site, return to Building Project home page and click on photo with this symbol in the middle

August 17-20, 2020

Going on this week: Setting cement block foundation



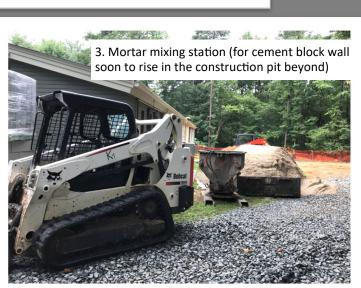











To see a video of the construction site, return to Building Project home page and click on photo with this symbol in the middle

August 13, 2020


Going on this week: concrete footings get poured; start setting cement blocks









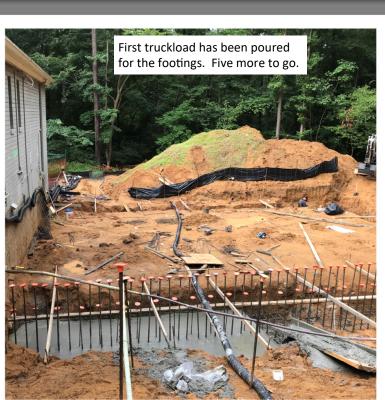

August 7, 2020

Going on this week: setting up the rebar and pouring the concrete footings

To see a video of the construction site, return to Building Project home page and click on photo with this symbol in the middle







To see a video of the construction site, return to Building Project home page and click on photo with this symbol in middle

July 30, 2020

Going on this week: moving excavated dirt out of the way (for foundation)







- ⇒ Go scoop dirt from the pile.
- ⇒ Trundle it along the outer rim of the construction site.
- \Rightarrow Dump the dirt into waiting truck.
- \Rightarrow Repeat.





To see a video of the construction site, return to Building Project home page and click on photo with this symbol in middle

July 23, 2020

Going on this week: preparing the slab site for pouring the footings

Views looking S from back (kitchen side) of Jones Bldg









2. Beyond that, high on the far west

digger beside another pile of dirt.

rim of the dug-out site, there's a white

To see a panorama of the construction site, return to Building Project home page and click on photo with this symbol in middle



July 16, 2020

Going on this week: more dirt moving, drainage measures









3 views from Jones Bldg SW corner (from playground outside lower level classrooms)



To see a VIDEO view of the construction site, return to Building Project home page and click on photo with this symbol in middle

July 9, 2020

Going on this week:
Erosion control,
utility relocation,
and grading for
building pad

2 views from Jones Bldg west side (just outside kitchen window)













July 1, 2020

This week: digging to find underground pipes'n'stuff—
See what the site looks like, here!



To see a VIDEO view of the construction site, return to Building Project home page and click on photo with this symbol in middle



3 views from alcove doors (between kitchen and stage)

For earlier photos, return to base page and click on Photo Gallery "IIA"
