



The Gallery pages below scroll backward in time.



Interior view towards N end of Multi-Purpose Room

February 25, 2021

*Going on this week:
Most exterior window
glass now installed;
taping and "mudding"
of drywall is moving
quickly.*

To see this week's video of the construction site, return to Building Project home page and click on photo with this symbol in the middle.



Composite interior view towards S end of Multi-Purpose Room





Window glass as delivered

To see this week's video of the construction site, return to Building Project home page and click on photo with this symbol in the middle.



February 17, 2021

Going on this week: Window glass has been delivered and is being installed!



Window glass Gallery N wall

Window glass Living Room S wall, exterior



Window glass at MultiPurpose Room entrance

Window glass Living Room S wall, interior





Corner Window

Tuesday, facing West wall of Multi-Purpose Room


Tuesday, facing East wall of Multi-Purpose Room



(Closet)



(Closet)

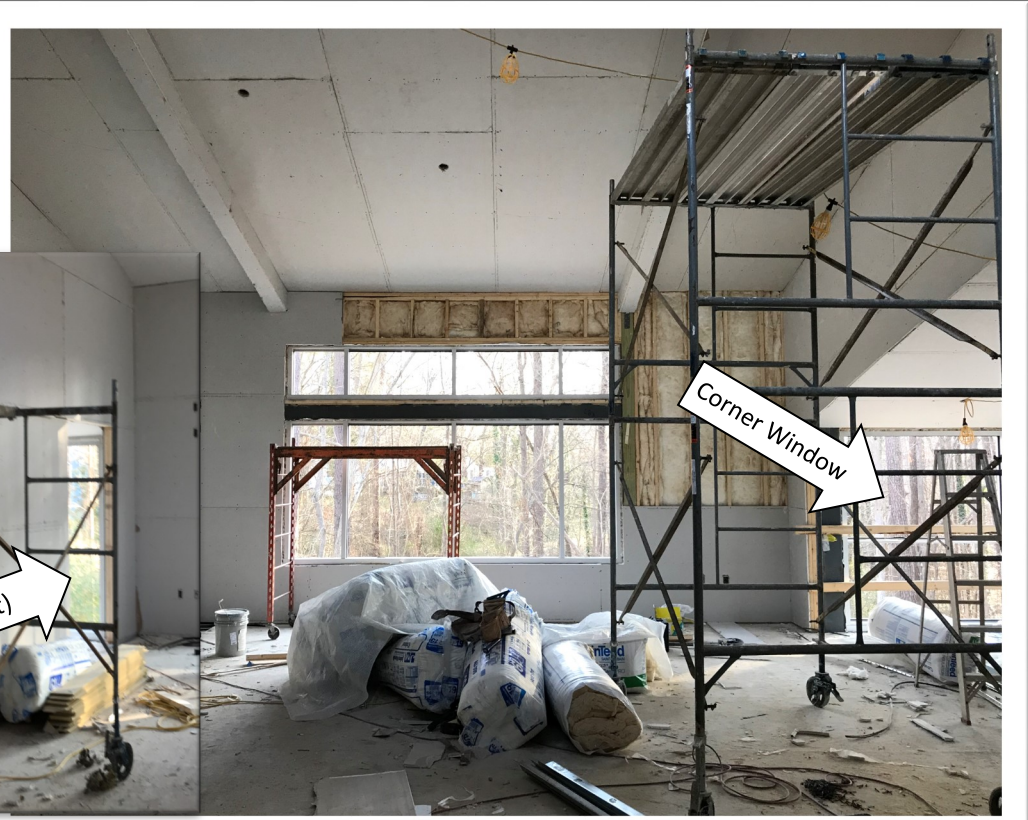

Corner Window


Wednesday, facing South wall of Multi-Purpose Room

To see this week's video of the construction site, return to Building Project home page and click on photo with this symbol in the middle.



February 9-10, 2021

Going on this week: Great progress with wall insulation and sheetrock installing!

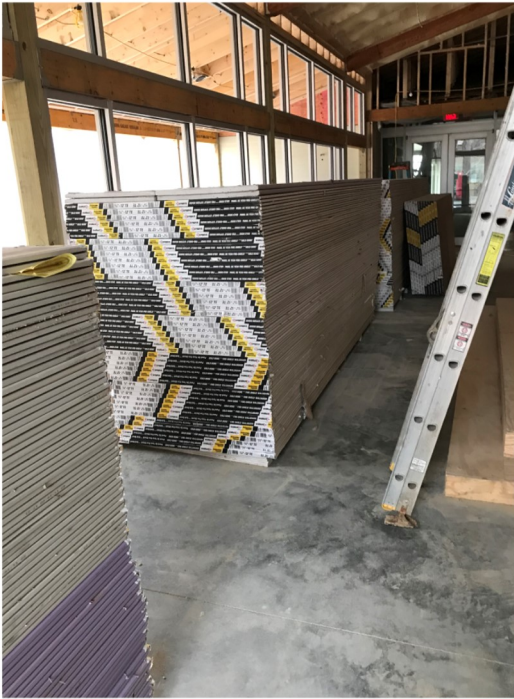

To see this week's video of the construction site, return to Building Project home page and click on photo with this symbol in middle.



February 4, 2021

Going on this week: Wall insulation and sheetrock panels are on site, awaiting delivery of windows. Meanwhile, exterior painting under way!



Exterior from SW



Exterior North face



Window frames between Gallery (inside) and Porch (outside)



Multi-Purpose Room

To see this week's video of the construction site, return to Building Project home page and click on photo with this symbol in the middle.



January 27, 2021

*Going on this week:
Window frames!
Ceiling insulation!*



In passageway at top of stairs down to Living Room on lower level

Sindy Barker and Brad Kosiba
conferring on progress



To see this week's video of the construction site, return to Building Project home page and click on photo with this symbol in the middle.



January 18, 2021

*Going on this week:
Volunteers anoint
plywood sheathing in
Multi-Purpose Room
with 400 names sig-
nifying congregants'
endorsement of our
new space!*

*Work continues to
fine-tune electrical &
mechanical rough-ins
in anticipation of
pending inspections.*



Rowan Marshall and Mary LeMay
writing on the east wall



Anna Waller
writing on the south wall

January 13, 2021



Late afternoon view of Exterior from SW

*Going on this week:
Nearing completion
of exterior siding,
trim & masonry;
Interior mechanical &
electrical rough-ins
awaiting inspection;
Walls readied for pre-
sheetrock signatures*

To see this week's video of the construction site, return to Building Project home page and click on photo with this symbol in the middle



View of MultiPurpose Room looking North/NW

FIRST LOOK! From Stage Level of old building west, through the passageway to the MultiPurpose Room



January 7, 2021

Going on this week: Final stages of exterior siding, trim and masonry; Continuation of interior mechanical & electrical/Wi-Fi rough-ins, and HVAC duct installation and insulation.

To see this week's video of the construction site, return to Building Project home page and click on photo with this symbol in the middle



View of South Exterior



View from Living Room looking South/SW



All quiet on the Northern front

*For earlier photos, return to base page
and click on Photo Gallery “IIA” for Jan-Jun 2020,
“IIB” for Jul-Aug 2020, “IIC” for Sep-Oct 2020, or
“IID” for Nov-Dec 2020*
